


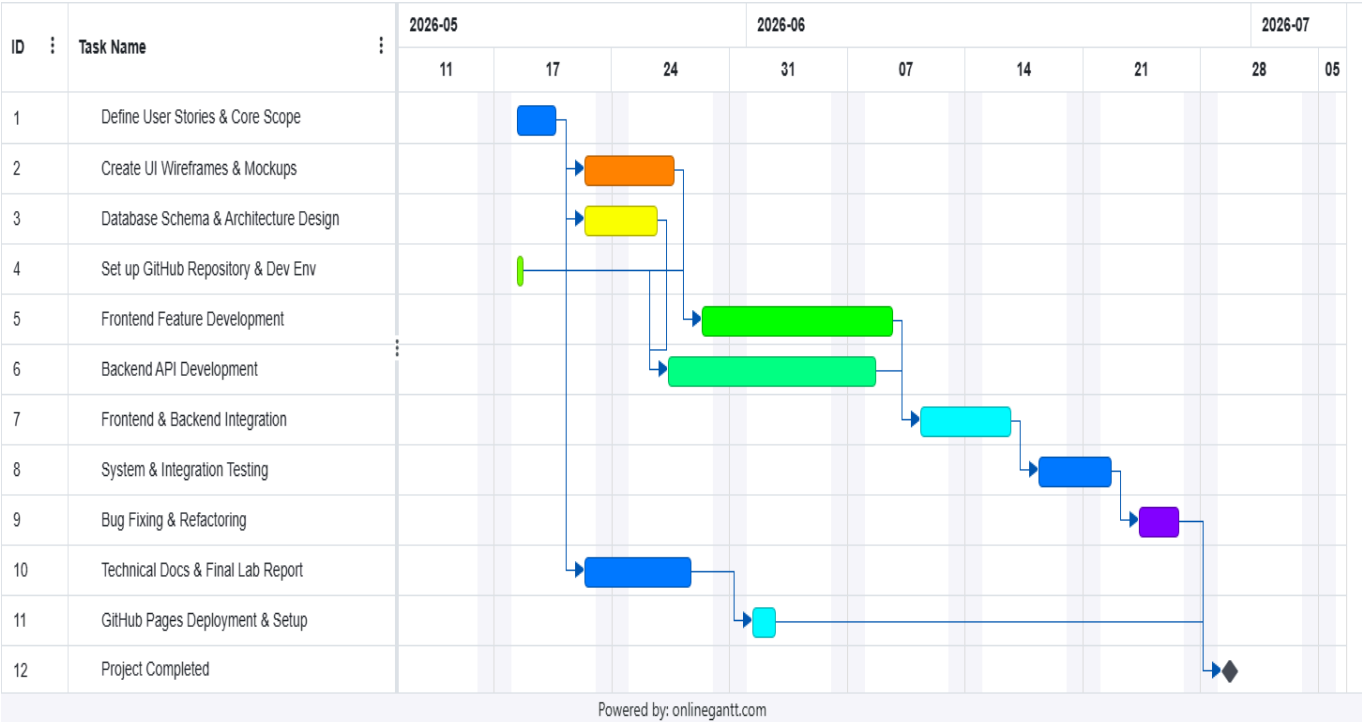

Task ID	Task Name	Duration (Days)	Dependencies	Assigned To	Notes / Assumptions
P1	Define User Stories & Core Scope	3	—	All Members	Collaborative kickoff phase
P2	Create UI Wireframes & Mockups	4	P1	Member A	Establishes the visual layout
P3	Database Schema & Architecture Design	3	P1	Member B	Maps backend entities and API routes
P4	Set up GitHub Repository & Dev Env	1	—	Member C	Can be done concurrently with design

P5	Frontend Feature Development	8	P2, P4	Member A & D	Building UI components
P6	Backend API Development	9	P3, P4	Member B & C	Building server logic and endpoints
P7	Frontend & Backend Integration	4	P5, P6	Member A & B	Connecting client side to database
P8	System & Integration Testing	3	P7	Member C & D	Validating end-to-end user flows
P9	Bug Fixing & Refactoring	3	P8	All Members	Polishing features based on test bugs
P10	Technical Docs & Final Lab Report	5	P1	Member D	Starts early, finalized alongside testing
P11	GitHub Pages Deployment & Setup	2	P10	Member C	Deploying the project plan page
M1	Project Completed	0	P9, P11	Milestone	Final project submission ready
